


PROVIDING UNDERGROUND SEWERAGE SCHEME TO AMBATTUR – PACKAGE – III IN CHENNAI CITY

- Ambattur is a newly added area among the 42 local bodies added in the expanded area of Chennai city which falls in Greater Chennai Corporation Divisions 84 to 93 in Area 7 (Ambattur) to an extent of 40.36 Sq.Km for a total length of about 554.64km.
- The Sewerage scheme for this Area has now been designed for a design period of 35 years from 2004-2039. The ultimate population to be served has been estimated as 8.83 lakhs. The ultimate waste water generation is projected as 106.08 MLD.

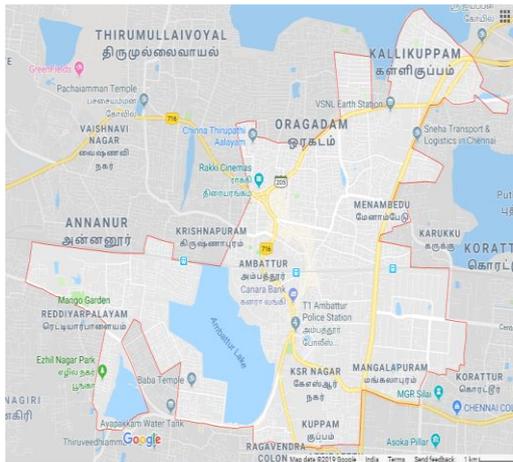

- The scheme cost for “Providing Underground Sewerage Scheme to Ambattur, Phase – III, Pkg-II (Bal.works) – Package - V” was sanctioned by the Central sanctioning and monitoring Committee of JNNURM on 29.02.2008 for Rs. 130.91 Crore.

- The Board accorded the administrative approval vide resolution No.124/2008, dated 18.06.2008.
- For the scheme the balance amount of ULB contribution sanctioned as per Grant under CMCDM 15-16 fund vide G.O. (MS) No.29, MAWS (M.C.I) Dept dt.10.2.2016.
- The work of providing sewerage facilities to Ambattur carried out by CMWSSB in 3 Phases, out of which Phase-I and Phase-II are completed. In Phase-III, out of 4 packages, 3 packages were completed and put into public use. The work under Package-II, the contract was terminated due to slow progress of work on 10.06.2016. The balance works in Package-II was split up in to six packages viz. Package – I to VI.

➤ The work of Providing sewerage facilities to Ambattur, Phase –III, Pkg –II (Bal. works) – Package – III falls in Ambattur, Division 84,85 &86 in Area 7 (Ambattur) covering 155 streets for a total length of 8.19km.

➤ **The components of work**

- | | |
|---|------------|
| 1. Laying of sewer gravity main | -8193 m |
| 2. Construction of Manholes | - 235nos |
| 3. Laying of pumping main | - 1542.36m |
| 4. Providing House Service Connections | - 173 nos |
| 5. Construction of sewage pumping stations- 2 nos and lift station - 1no. | |

➤ **Contract details**

The work has been awarded to Th. G. Shirangarayan for a contract value of Rs. 1096.50 lakhs on 18.01.2019 with a contract period of 18 months. The work was commenced on 18.02.2019.

➤ The work was completed and inaugurated on 23.02.2021 and put into public use.
